

Sprint 1 Report

ClassMate 1/30/25

Actions to stop doing

Although it's not a frequent issue, some team members aren't able to make meetings consistently and we hope that this won't occur as much going forward. We also need to make sure our Scrum meetings don't go over the allocated 15 minutes.

Actions to start doing

The team should resolve to have clearer communication between team members regarding our task assignments and completion. This sprint was not as productive as it could have been because not all members of the development team were clear on what they should do, what had already been done, and what was currently being done. A related issue was that the tasks we created weren't super clear in their wording, making it hard for people to figure out exactly what they should do for their assigned tasks. For future sprints, we will make sure that subteams have strong communication, starting by making sure all team members are sufficiently onboarded, and understand all of the technologies and workflows of their subteam. We will also resolve to update our jira scrum board more frequently to more accurately reflect our current progress in the sprint. Additionally, we should begin having more frequent group work sessions, to more efficiently work on our product.

Actions to keep doing

We should continue to be active in the group server to maintain lines of communication for our meetings and document writing. Furthermore, we should continue using GitHub and tools like Figma to make the development process smoother. For example, by having clear commit messages to make it easier to understand changes made to the development branch. Team members have also done a good job of learning their spikes and applying the knowledge to their tasks.

Work Completed

During Sprint One, we managed to complete our first user story, which involved implementing the frontend and backend systems for the registration and login functionality of our website. For the frontend, we created the landing, registration, and login pages and have Figma designs for the profile and explore page UIs. As for the backend, We also managed to

overcome our learning spikes for this sprint, and are now overall much more familiar with the technologies we are using.

Work Not Completed


We have not completed all of the tasks created for our second user story, which was concerned with creating a user profile. We are also yet to link the frontend to the database, and we need to ensure that login/registration fully works before proceeding to the next tasks.

Work Completion Rate

Task	Status
Set up backend for user authentication and registration	Completed
Allow users to register using email and create an account	Completed
Create frontend UI for login and registration	Completed
Design and develop the post-login landing page	Partial
Implement profile editor frontend that allows users to add/edit their bio	Incomplete
Develop backend support for user profiles	Incomplete
Design and build the profile page UI	Partial

Burnup Chart

Total Story Points and Cumulative Completed

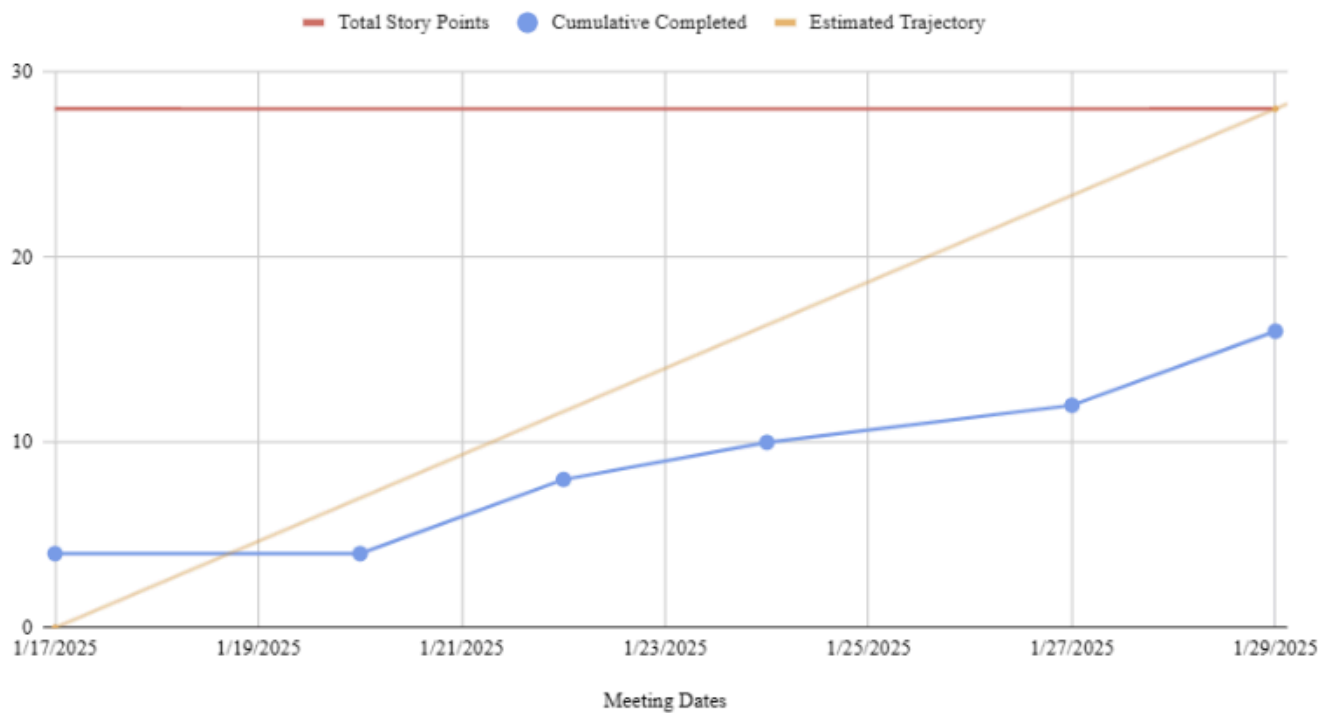

SPRINT 1	
Completion Rate (Points/Day)	1.14
Total User Stories Completed	1
Total Work Done (Story Points)	16
Total Days in Sprint	14
Sprint Completion Percentage	57.14%
